



US Army Corps
of Engineers.

MCCORMICK PLACE HALL A - CHICAGO, IL

ARENA TO HEALTHCARE (A2HC)




McCormick Place Hall A

Location: Chicago, IL
MSC: Great Lakes and Ohio River Division (LRD)
FEMA Region: V
FEMA MA (\$): \$15M
Type: Arena (A2HC)
Patient Type: COVID-19
Facility Size: 840,000 SF
Beds: 1750 low acuity beds



2301 S King Dr. West 34 St. Chicago, IL 60616

Planned

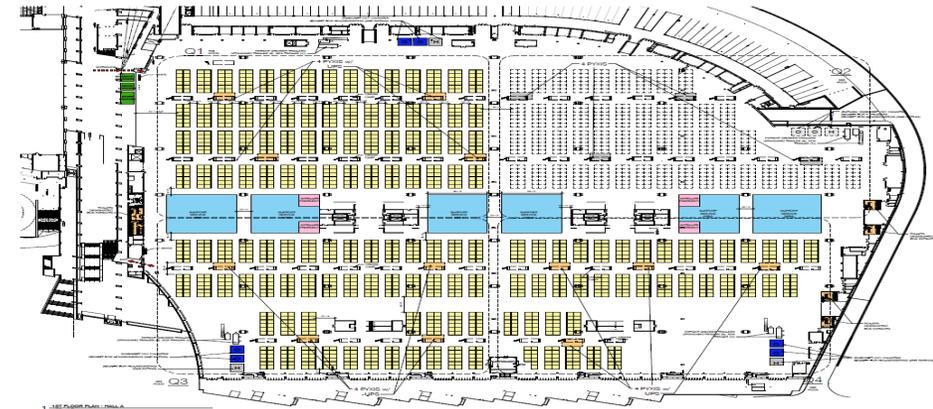


Construction Timeline

Assessment MA received	26 March 20
Construction MA received	26 March 20
Contract Awarded/NTP	28 March 20
Construction Start	29 March 20
Required Delivery	24 April 20
Estimated Completion	24 April 20
Actual Completion	
Total Days	27 days
Days Early/Late	


In progress, 0 % complete

Projection of COVID-19 Cases by 20 April 20

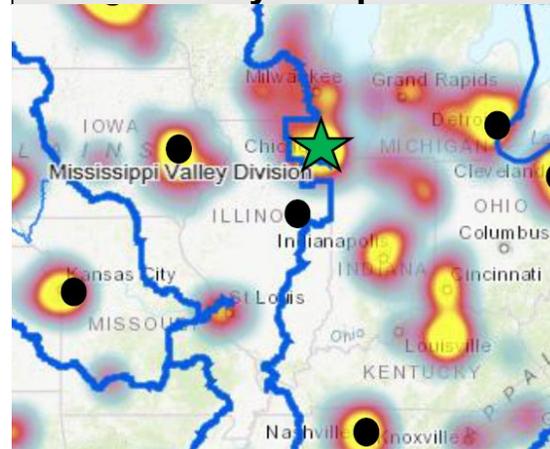

Anticipated peak of COVID-19 cases in the Chicagoland area is estimated to be by 20 April 2020.

In Progress

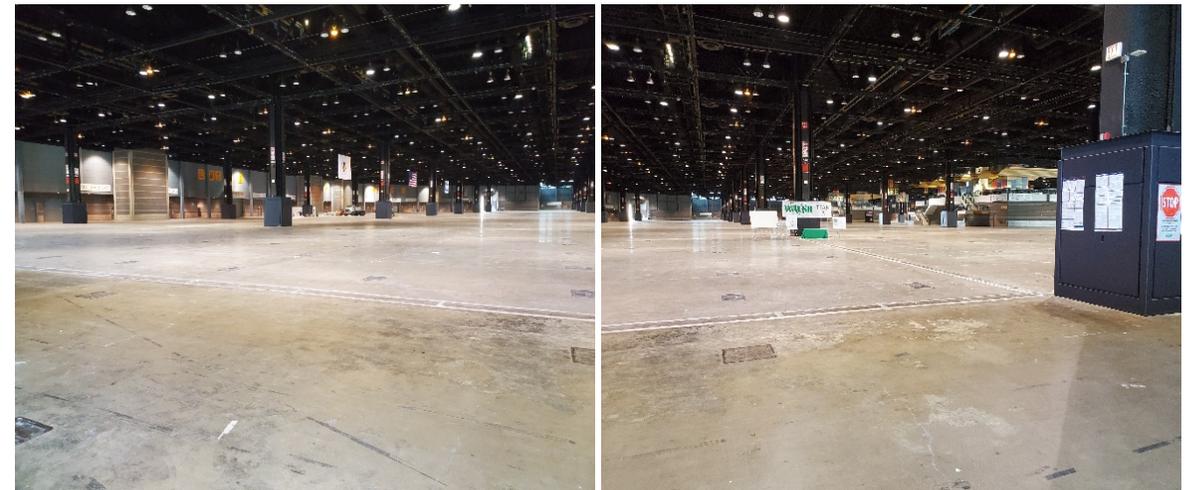

Supplies and equipment set up in corner of Hall A (2 April 2020).



US Army Corps of Engineers.

MCCORMICK PLACE HALL B - CHICAGO, IL ARENA TO HEALTHCARE (A2HC)




McCormick Place Hall B

Location: Chicago, IL
MSC: Great Lakes and Ohio River Division (LRD)
FEMA Region: V
FEMA MA (\$): \$15M
Type: Arena (A2HC)
Patient Type: COVID-19
Facility Size: 496,000 sq ft
Beds: 750 medium acuity beds



2301 S King Dr. West 34 St. Chicago, IL 60616

Planned

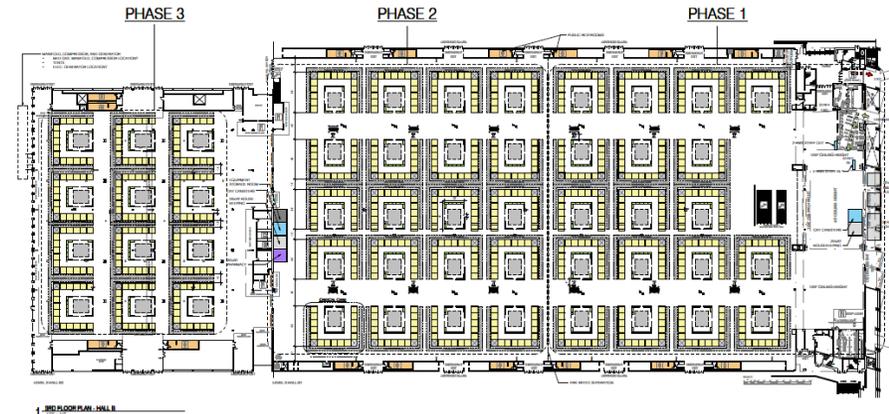


Construction Timeline

Assessment MA received	26 March 20
Construction MA received	26 March 20
Contract Awarded/NTP	28 March 20
Construction Start	29 March 20
Required Delivery	24 April 20
Estimated Completion	24 April 20
Actual Completion	
Total Days	27 days
Days Early/Late	


In Progress, 0 % Complete

Projection of COVID-19 Cases by 20 April 20

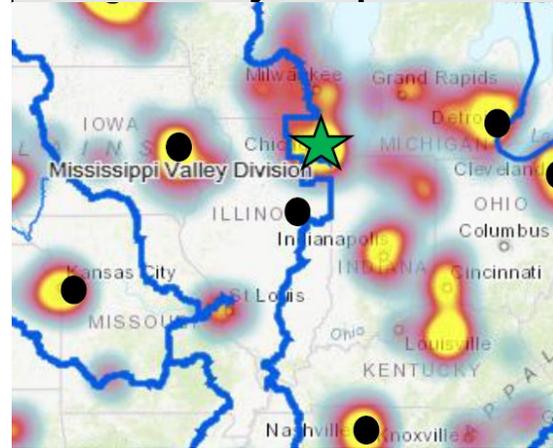

Anticipated peak of COVID-19 cases in the Chicagoland area is estimated to be by 20 April 2020.

In Progress

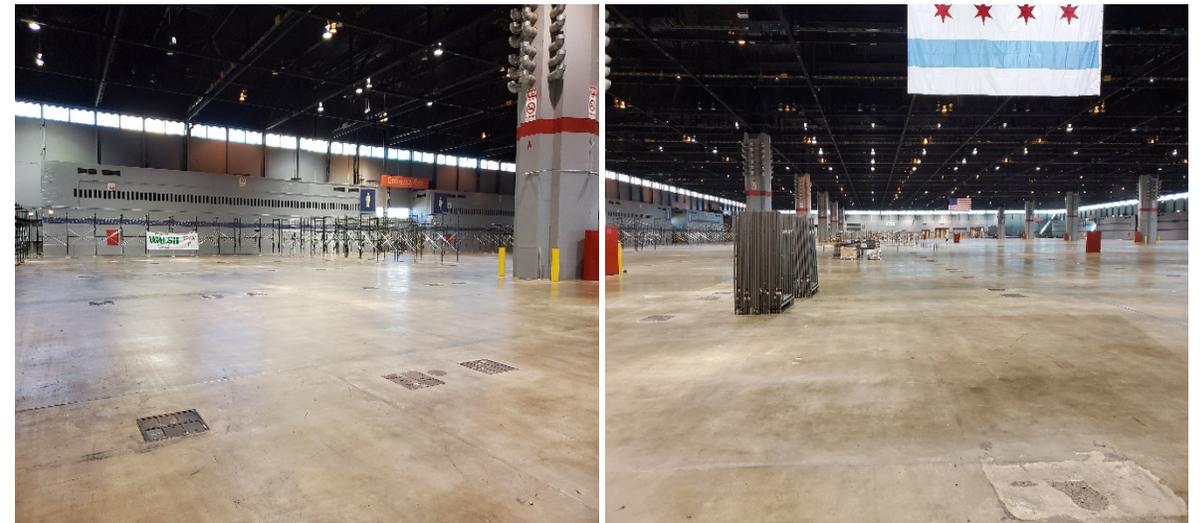

Construction areas laid out; scaffolding set up (2 April 2020).



US Army Corps
of Engineers.

MCCORMICK PLACE HALL C - CHICAGO, IL

ARENA TO HEALTHCARE (A2HC)



McCormick Place Hall C

Location: Chicago, IL
MSC: Great Lakes and Ohio River Division (LRD)
FEMA Region: V
FEMA MA (\$): \$15M
Type: Arena (A2HC)
Patient Type: COVID-19
Facility Size: 209,500 sq ft
Beds: 500 low acuity beds



2301 S King Dr. West 34 St. Chicago, IL 60616

Planned




Construction Timeline

Assessment MA received	26 March 20
Construction MA received	26 March 20
Contract Awarded/NTP	28 March 20
Construction Start	29 March 20
Required Delivery	03 April 20
Estimated Completion	03 April 20
Actual Completion	
Total Days	27 days
Days Early/Late	



97% complete; 100% expected on 03 APR

Projection of COVID-19 Cases by 20 April 20

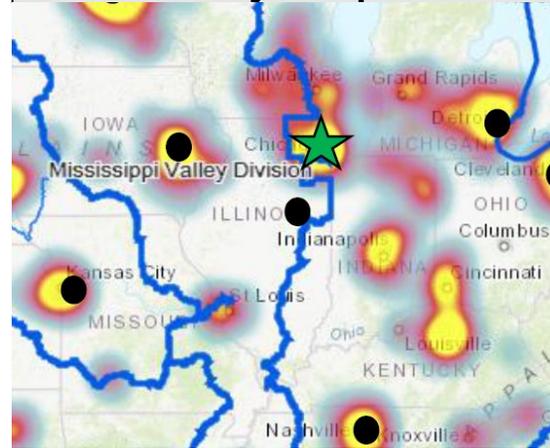

Anticipated peak of COVID-19 cases in the Chicagoland area is estimated to be by 20 April 2020.

In Progress

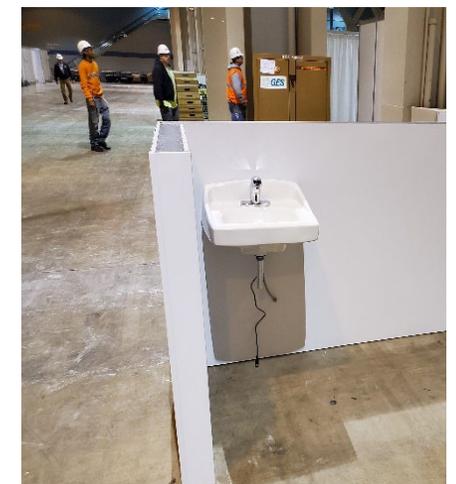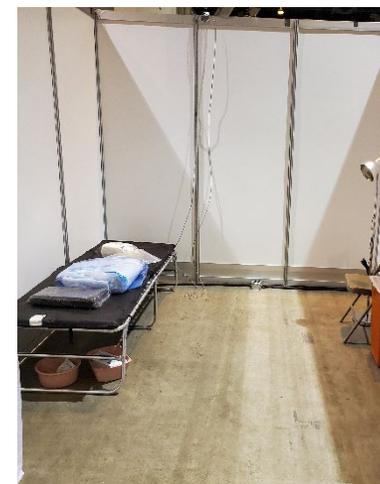

Illinois Air National Guard and contractors continue setting up FMS (2 April 2020).
